




Progress at the wind site

With regards to the reports given by the Engineers of Wind International Design and Property Development, the deadline of Jumeirah Lakes Towers is end of the year 2008.

During the previous week the supervision was done by the Consultant and it was approved. The inspection however was finally done by JAFZA and it was approved and currently arrival of the concrete is awaited.

The amount of concrete to be poured for the foundation is 4,500 m³ which equals to the amount of concrete used to build a 20 storey building. The Wind Management is optimistic about the foundation process, which is due to take place this week.

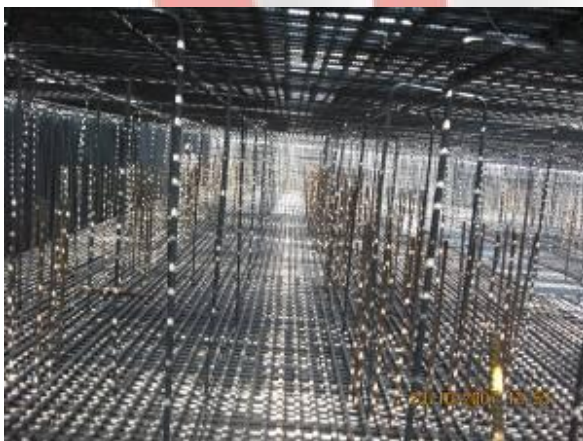

Reinforcement Wind Tower II

During the week that went by the reinforcement continued at Wind Tower II. The supervision was finally done and approved by the consultant, and the inspection which was done by JAFZA has been approved, where once the concrete is received, the raft foundation will be poured.



Material Received for reinforcement Wind Tower II




Reinforcement Wind Tower II

Pictures of the Week

Wind Tower I

<http://www.faravand.org/wind%20process/process%20page.htm>

Wind Tower II

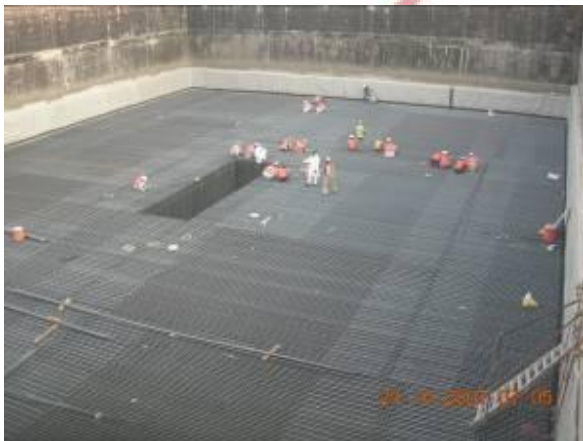

Reinforcement Wind Tower II



Reinforcement Wind Tower II

<http://www.faravand.org/wind%20process/process%20pageII.htm>



Reinforcement Wind Tower II
