



With regards to the reports given by the Engineers of Wind International Design and Property Development, the deadline of Jumeirah Lakes Towers is end of the year 2008.

WIND TOWER I

Last week on 13.12.2007 concrete casting of Wind Tower I started, around 3000 cubic meter of concrete was poured & casting of the floor of basement 5 finished at 2:00 a.m 14.12.07.



Concrete pouring of Wind Tower I

Curing is under progress till Thursday 20.12.07. Shuttering of the central core & columns has finished & ready for casting which will be done today.



Shuttering of central core finished, wind Tower I

WIND TOWER II

On 07.12.07 casting of Wind tower II for the floor of the basement 3 has finished. Stage of curing also finished.



Curing of Wind Tower II

Scaffolding installation for plastering is finished. Plastering started on 15.02.07, when finishes water proofing will start. Climbing shuttering fabrication is in the progress for central core casting.



Scaffolding & plastering of Wind Tower II

To view more videos go to:

www.windtower.net


Pictures of the week:



Concrete pouring Wind Tower I



Concrete pouring Wind Tower I

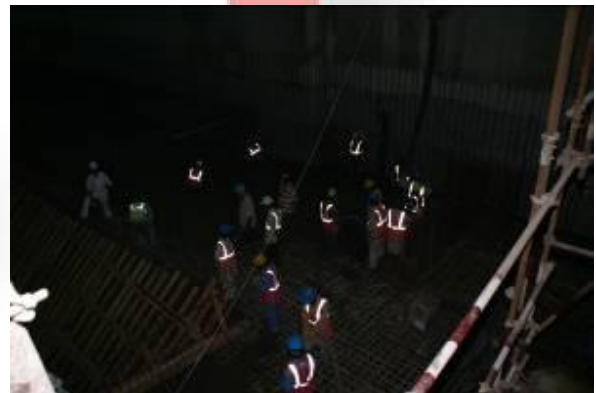

Night shift Wind Tower I, concrete pouring

For more picture & videos kindly click on the links below:

<http://www.faravand.org/wind%20process/process%20page.htm>

<http://www.faravand.org/wind%20process/process%20pageII.htm>
