



Int'l Design & Property Development Inc.

We had discontinued the newsletter update for some time since we gave priority to our websites and forums; but due to high demand, we have decided to continue the newsletter from where we left off.

WIND TOWER I

- Concrete Casting of level 23.13 has been completed.
- Steel Installation of vertical elements level 23.13 to level 26.09 has been completed.
- Steel prefabrication of vertical elements level 26.09 to level 29.05 is in progress.
- Steel cut and bending for vertical elements level 29.05 to level 32.01 is in progress.
- Steel supply of 6 floors will soon arrive at site.



Wind Tower I

WIND TOWER II

- Concrete casting of level 23.41 has been completed.
- Steel installation of vertical elements level 23.41 to level 26.42 has been completed.
- Steel Prefabrication of vertical elements level 26.42 to level 29.43 is in progress.
- Steel cut and bending of vertical elements level 29.43 to 32.44 is in progress.
- Steel supply for 6 floors will soon arrive at site.



Wind Tower II

***** WE ARE PROUD TO ANNOUNCE THAT OUR COMPANY HAS BEEN LISTED AMONG THE APPROVED LIST OF DEVELOPERS IN U.A.E. CODE No. 254, ESCROW ACCOUNT HAS BEEN OPENED**

For more detail go to the following link:

<http://www.farayand.ae/Wind%20Photo/scan0002.jpg>

[List of RERA Approved Developers](#)

To view more videos go to:

www.windtower.net


<http://www.youtube.com/WindSpokesperson>

For more picture & videos kindly click on the links below:


[Wind Tower I](#)

[Wind Tower II](#)

**Wind Tower I
Progress Graph**

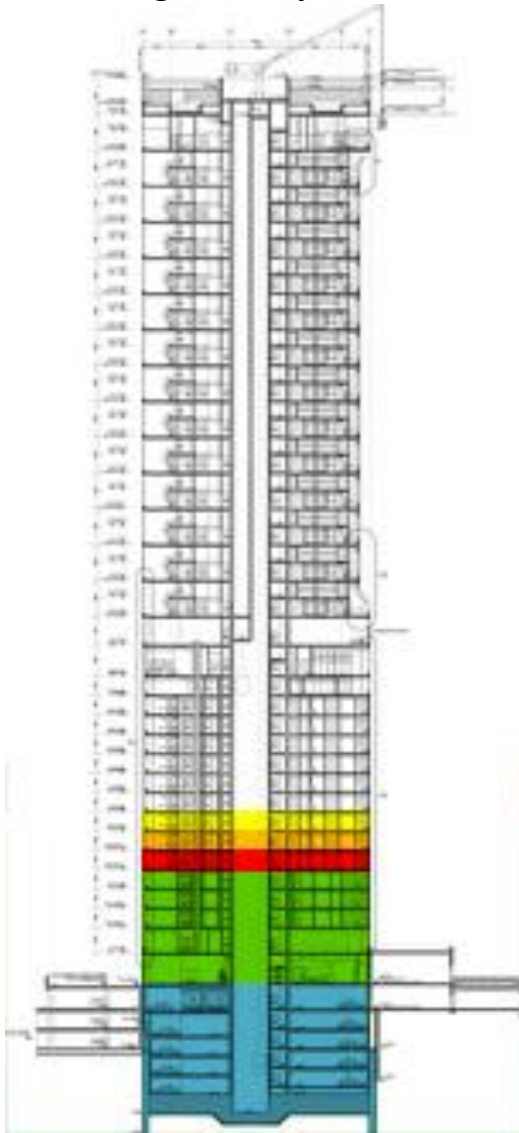

**Wind Tower II
Progress Graph**

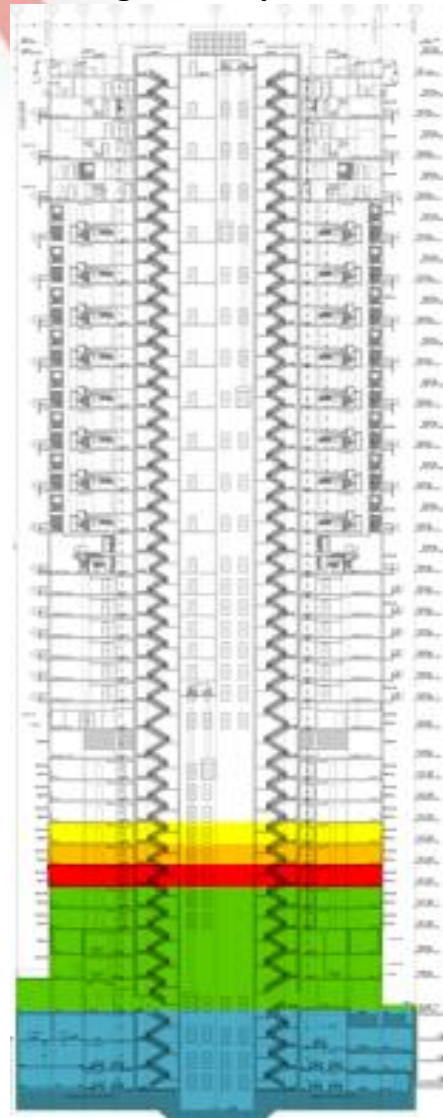

Graph Legend

- Steel Cut and Bend
- Steel Prefabrication
- Steel Installation
- Concrete Casting
- Block Work and Finishing
